PerfectMatch

Beatrice Maria Giurgica, C23703949

Contents

1. Technical Scope & Concept
2. System Architecture
3. Market & Potential End Users
4. Marketing Project Plan
5. Resources & Costs
6. Potential Risks

1. TECHNICAL SCOPE & CONCEPT

1. 1 System Concept

- Mobile app for personalised beauty
- Uses AI for skin analysis
- AR tools for virtual try-ons
- Ingredient safety checking system
- Product comparison features
- Supports skincare, makeup, grooming
- Designed for consumers & dermatologists

1. 2 Technical Scope

- Consumer is main system user
- 4 core functions included:
  - AI-generated personalised routines
  - AR makeup and product try-on
  - Ingredient safety checking
  - Compare multiple selected products

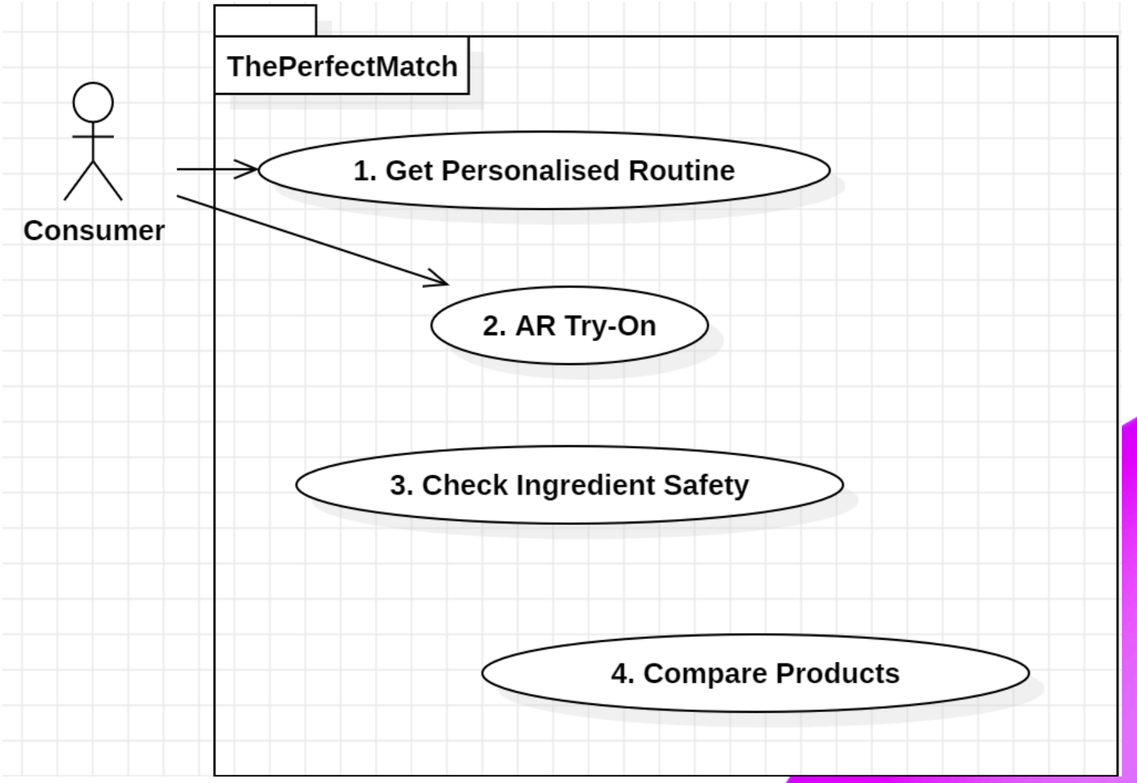

1. 3 Requirements & Feasibility Metrics

Functional Requirements

- Generate personalised AI routines
- Provide AR product try-on
- Check ingredient safety
- Compare products by criteria
- Display verified product data
- Save user routines securely
- Support simple mobile UI

Non-Functional Requirements

- AI routine under 5 seconds
- AR loads within 2 seconds
- Product searches under 3 seconds
- System uptime 99.9%
- Full GDPR compliance
- Secure data encryption
- Works on iOS & Android

2. SYSTEM ARCHITECTURE

2. 1 Architecture Diagram

- Client-server Architecture
- App connects through API gateway
  - AI engine handles routine generation
  - AR service manages virtual try-ons
  - Product database stores verified data
- Scalable cloud-based architecture
  - Backend processes comparisons

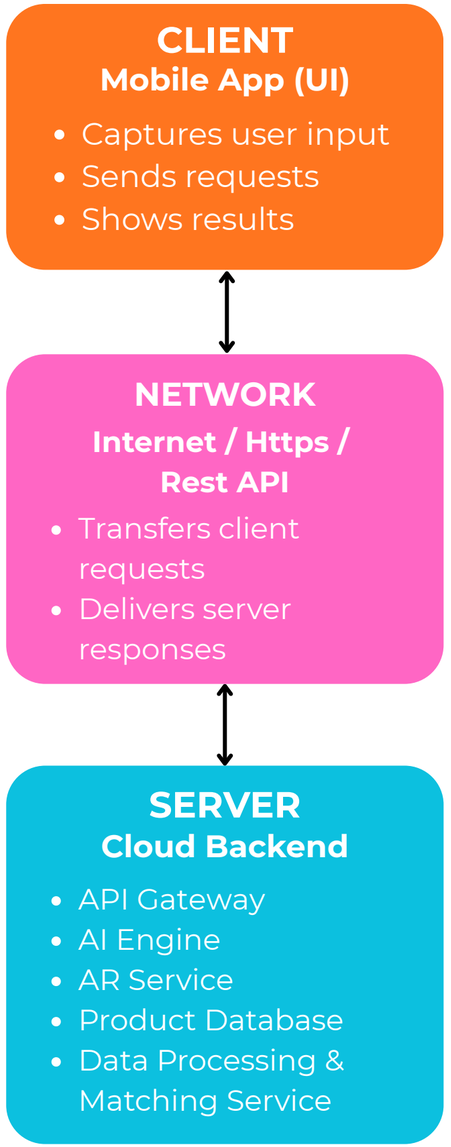

3. MARKET & POTENTIAL END USERS

3. 1 Beauty Market Overview

- Smartphone adoption above 85% in Europe
- Highest usage in 18–34 age group
- Beauty purchases shifting strongly online
- Over 40% buy skincare digitally monthly
- Growing use of AI and AR tools
- Consumers rely on apps for product decisions
- Strong demand for personalised beauty solutions

3. 2 End Users & Stakeholders

- **General Consumers** seeking personalised routines
- **Dermatologists** offering expert feedback
- **Influencers** sharing routines and reviews
- **Beauty Brands** wanting visibility and data
- **Retailers** integrating product listings
- **System Administrators** managing platform services
- **Developers** maintaining AI and AR features

4. MARKETING PROJECT PLAN

4. 1 Mind Map

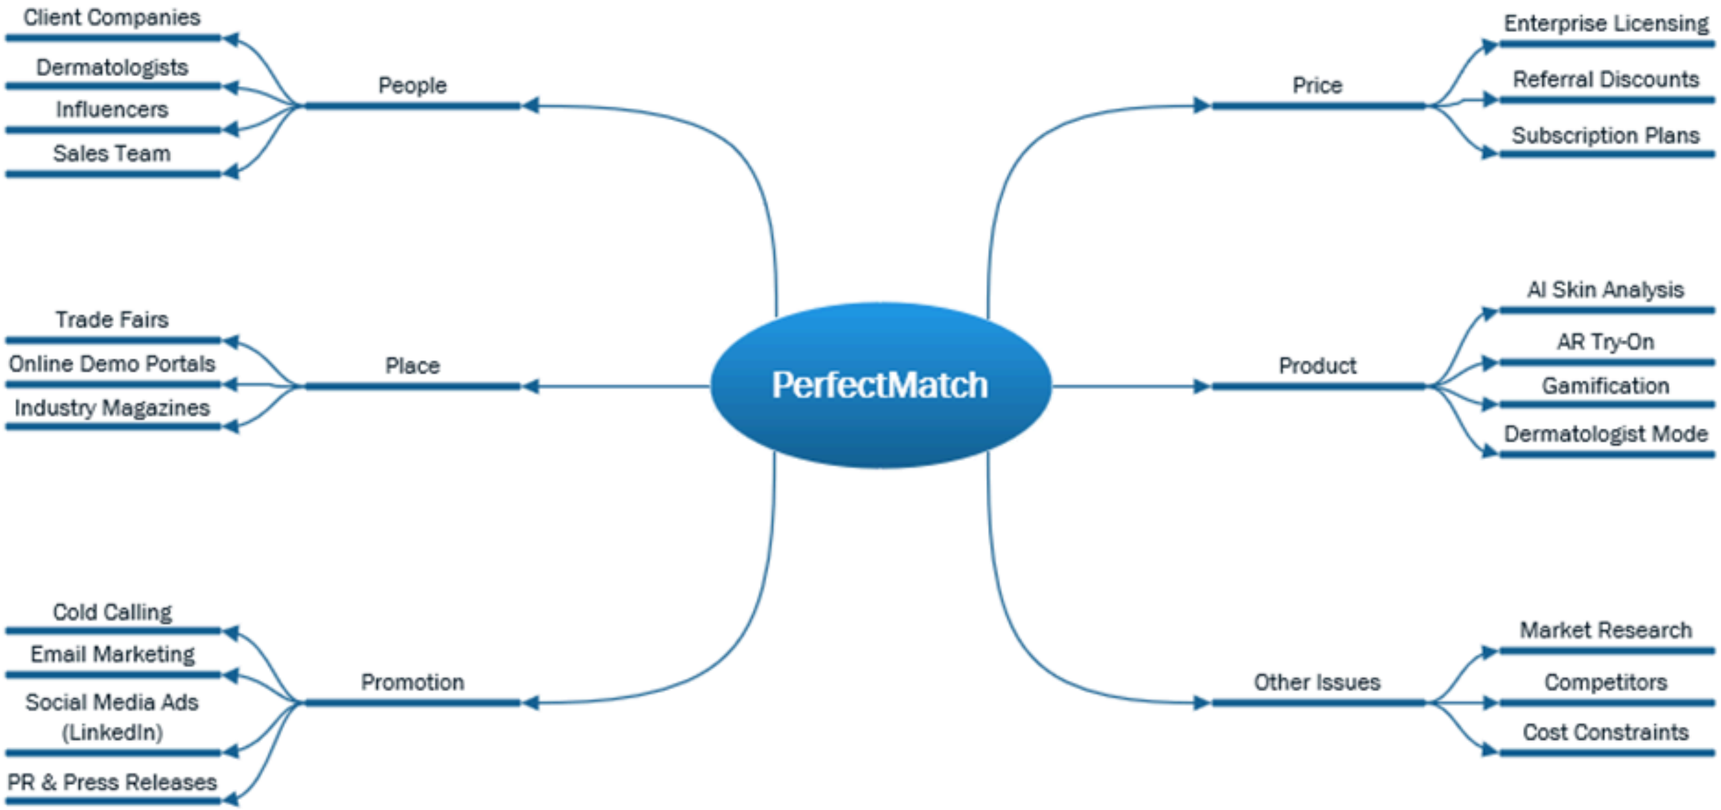
PerfectMatch
People
Client Companies
Dermatologists
Influencers
Sales Team
Place
Trade Fairs
Online Demo Portals
Industry Magazines
Promotion
Cold Calling
Email Marketing
Social Media Ads (LinkedIn)
PR & Press Releases
Price
Enterprise Licensing
Referral Discounts
Subscription Plans
Product
AI Skin Analysis
AR Try-On
Gamification
Dermatologist Mode
Other Issues
Market Research
Competitors
Cost Constraints

4. 2 Work Packages Overview

WP1

Marketing Strategy

- Analyse product features and positioning
- Build pricing and promotion plans
- Define distribution channels and approvals

WP2

Promotional Materials

- Produce email, brochure and PR content
- Create demo scripts and presentations
- Build online demo portal materials

WP3

Client Outreach & Engagement

- Identify and contact potential clients
- Organise demos and trade fair prep
- Collect client feedback and follow-up

4. 2 Work Packages Overview

WP4

Business & Pricing Model Development

- Research competitor pricing and models
- Define subscription tiers and discounts
- Prepare pricing sheets and documentation

WP5

Social Media Ads

- Select platforms and target audience
- Develop messaging and visual designs
- Launch ads and analyse performance

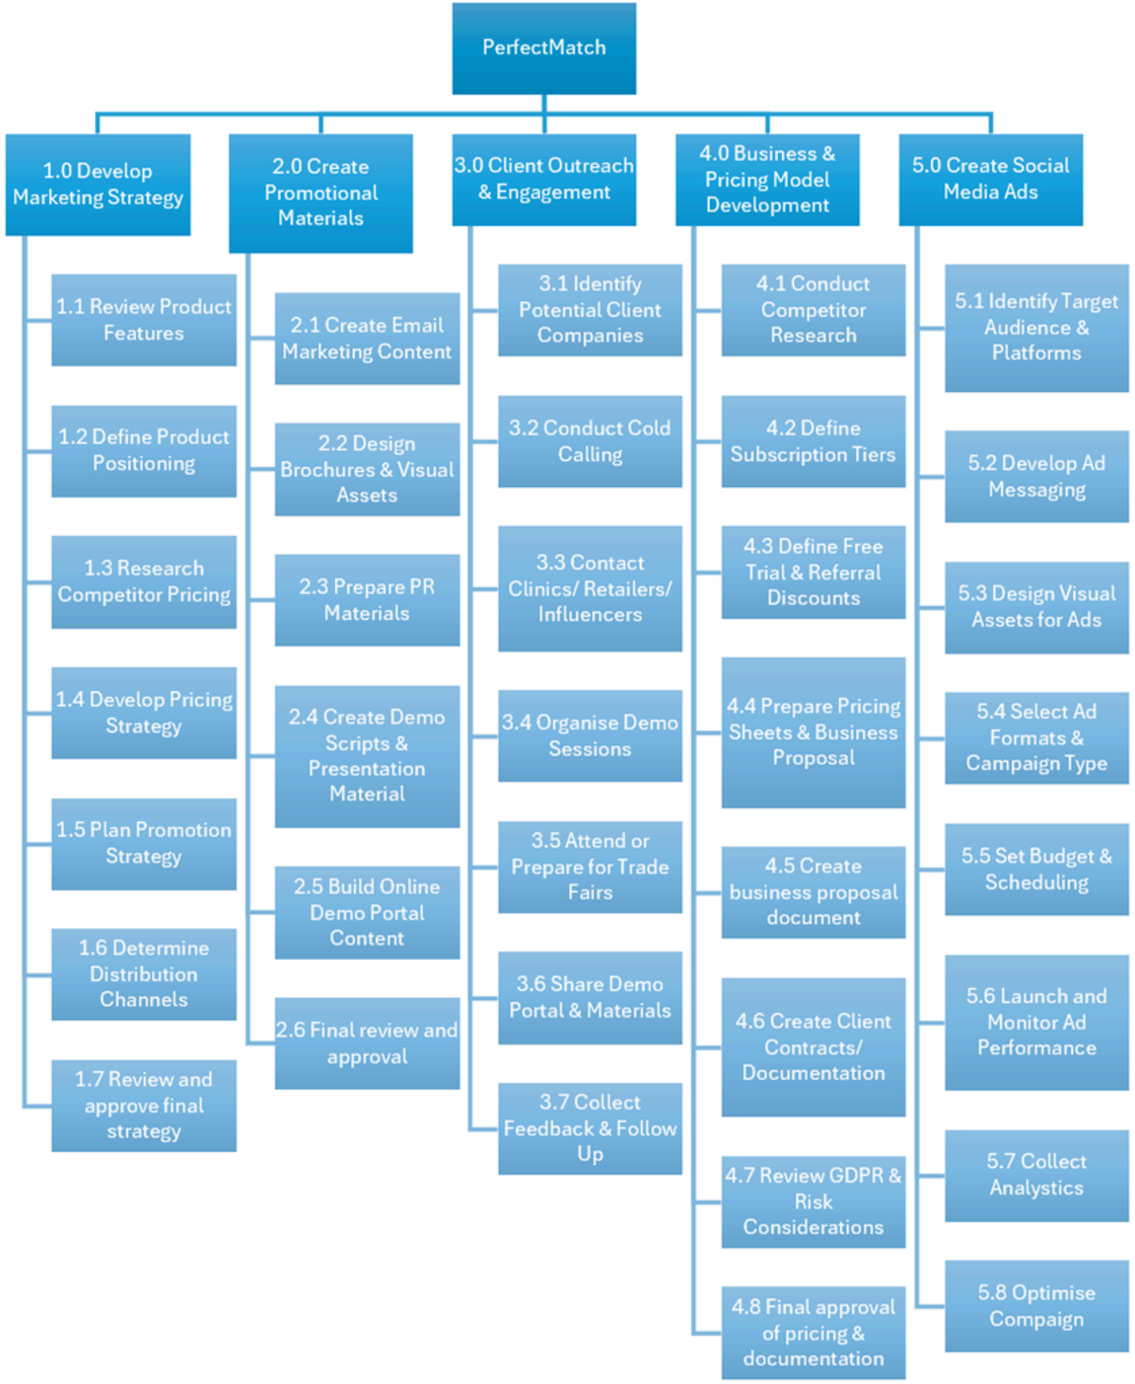
PerfectMatch
1.0 Develop Marketing Strategy
1.1 Review Product Features
1.2 Define Product Positioning
1.3 Research Competitor Pricing
1.4 Develop Pricing Strategy
1.5 Plan Promotion Strategy
1.6 Determine Distribution Channels
1.7 Review and approve final strategy
2.0 Create Promotional Materials
2.1 Create Email Marketing Content
2.2 Design Brochures & Visual Assets
2.3 Prepare PR Materials
2.4 Create Demo Scripts & Presentation Material
2.5 Build Online Demo Portal Content
2.6 Final review and approval
3.0 Client Outreach & Engagement
3.1 Identify Potential Client Companies
3.2 Conduct Cold Calling
3.3 Contact Clinics/ Retailers/ Influencers
3.4 Organise Demo Sessions
3.5 Attend or Prepare for Trade Fairs
3.6 Share Demo Portal & Materials
3.7 Collect Feedback & Follow Up
4.0 Business & Pricing Model Development
4.1 Conduct Competitor Research
4.2 Define Subscription Tiers
4.3 Define Free Trial & Referral Discounts
4.4 Prepare Pricing Sheets & Business Proposal
4.5 Create business proposal document
4.6 Create Client Contracts/ Documentation
4.7 Review GDPR & Risk Considerations
4.8 Final approval of pricing & documentation
5.0 Create Social Media Ads
5.1 Identify Target Audience & Platforms
5.2 Develop Ad Messaging
5.3 Design Visual Assets for Ads
5.4 Select Ad Formats & Campaign Type
5.5 Set Budget & Scheduling
5.6 Launch and Monitor Ad Performance
5.7 Collect Analystics
5.8 Optimise Compaign

4. 3 Gantt Chart

WP1 defines overall marketing direction

WP4 depends on WP1 outputs

WP2 needs messaging and pricing

WP5 follows completed promotional materials

WP3 needs materials and pricing

Task Name	Duration	Start	Finish	Predecesso	Resource Names	Add New Col
WP1 Develop Marketing Strategy	**12 days**	**Mon 01/06/26**	**Tue 16/06/26**			
1.1 Review system product features	1 day	Mon 01/06/26	Mon 01/06/26		Marketing Analyst	
1.2 Define product positioning	1 day	Tue 02/06/26	Tue 02/06/26	2	Marketing Lead	
1.3 Research competitor pricing	2 days	Wed 03/06/26	Thu 04/06/26	3	Marketing Intern	
1.4 Develop pricing strategy	2 days	Fri 05/06/26	Mon 08/06/26	4	Marketing Lead	
1.5 Plan promotional strategy	3 days	Tue 09/06/26	Thu 11/06/26	5	Marketing Team	
1.6 Determine distribution channels	2 days	Fri 12/06/26	Mon 15/06/26	6	Marketing Manager	
1.7 Review and approve final marketing strategy	1 day	Tue 16/06/26	Tue 16/06/26	7	All stakeholders	
WP1 Complete	0 days	Tue 16/06/26	Tue 16/06/26	8		

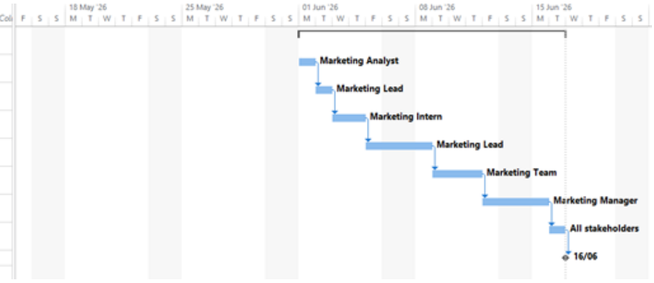

Task Name	Duration	Start	Finish	Predecesso	Resource Names	Add New Column
WP4 Business & Pricing Model Development	**16 days?**	**Wed 17/06/26**	**Wed 08/07/26**			
4.1 Conduct competitor pricing research	2 days	Wed 17/06/26	Thu 18/06/26		Marketing Analyst	
4.2 Define subscription tie	2 days	Fri 19/06/26	Mon 22/06/26	2	Marketing Lead	
4.3 Define free trial & referral discount policies	2 days	Tue 23/06/26	Wed 24/06/26	3	Marketing Lead	
4.4 Prepare pricing sheets	2 days	Thu 25/06/26	Fri 26/06/26	4	Marketing Analy	
4.5 Create business proposal document	3 days	Mon 29/06/26	Wed 01/07/26	5	Marketing Manager	
4.6 Draft client contract templates	2 days	Thu 02/07/26	Fri 03/07/26	6	Administrator	
4.7 Review GDPR compliance & identify	2 days	Mon 06/07/26	Tue 07/07/26	7	Project Supervisor	
4.8 Final approval of pricing & business	1 day	Wed 08/07/26	Wed 08/07/26	8	All stakeholders	
WP4 Complete	0 days	Wed 08/07/26	Wed 08/07/26	9		

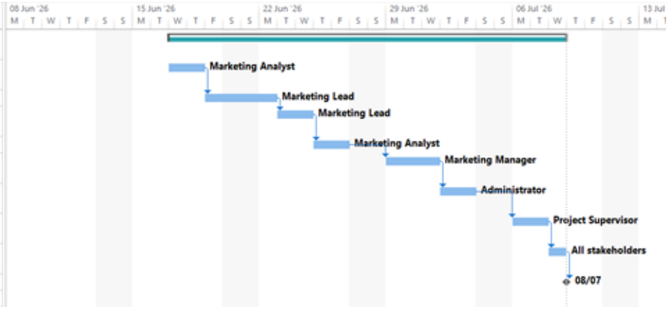

Task Name	Duration	Start	Finish	Predecesso	Resource Names	Add New Column
WP2 Create Promotional Material	**13 days**	**Thu 09/07/26**	**Mon 27/07/26**			
2.1 Write email marketing	2 days	Thu 09/07/26	Fri 10/07/26		Copywriter	
2.2 Design brochures & leaflets	3 days	Mon 13/07/26	Wed 15/07/26	2	Graphic Designer	
2.3 Prepare PR materials	2 days	Thu 16/07/26	Fri 17/07/26	3	PR Officer	
2.4 Write demo script & slide deck	2 days	Mon 20/07/26	Tue 21/07/26	4	Marketing Lead	
2.5 Build online demo portal content	3 days	Wed 22/07/26	Fri 24/07/26	5	Web Editor	
2.6 Final review and approval of all materials	1 day	Mon 27/07/26	Mon 27/07/26	6	Marketing Manager	
WP2 Complete	0 days	Mon 27/07/26	Mon 27/07/26	7		



Task Name	Duration	Start	Finish	Predecesso	Resource Names	Add New Column
WP5 Create Social Media Ads	**14 days**	**Tue 28/07/26**	**Fri 14/08/26**			
5.1 Identify target audience & select platforms	1 day	Tue 28/07/26	Tue 28/07/26		Marketing Analyst	
5.2 Develop ad messaging	2 days	Wed 29/07/26	Thu 30/07/26	2	Copywriter	
5.3 Design visual assets for ads	3 days	Fri 31/07/26	Tue 04/08/26	3	Graphic Designer	
5.4 Select ad formats & campaign type	1 day	Wed 05/08/26	Wed 05/08/26	4	Marketing Lead	
5.5 Set budget & scheduling	1 day	Thu 06/08/26	Thu 06/08/26	5	Marketing Manager	
5.6 Launch ad campaign & monitor performance	2 days	Fri 07/08/26	Mon 10/08/26	6	Social Media Coordinator	
5.7 Collect analytics	2 days	Tue 11/08/26	Wed 12/08/26	7	Marketing Analy	
5.8 Optimise campaign based on analytics	2 days	Thu 13/08/26	Fri 14/08/26	8	Social Media Coordinator	
WP5 Complete	0 days	Fri 14/08/26	Fri 14/08/26	9		

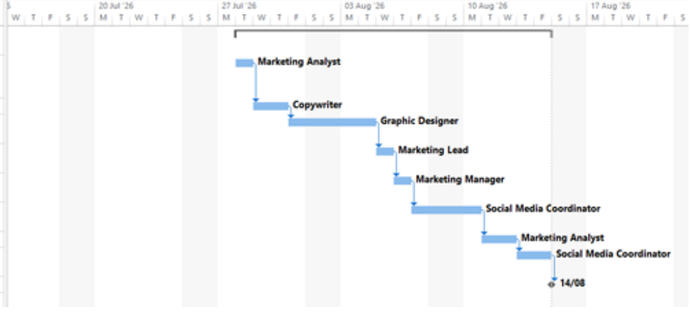

Task Name	Duration	Start	Finish	Predecesso	Resource Names	Add New Column
WP3 Client Outreach & Engagement	**15 days**	**Mon 17/08/26**	**Fri 04/09/26**			
3.1 Identify potential business clients	2 days	Mon 17/08/26	Tue 18/08/26		Marketing Assistant	
3.2 Conduct cold calling & outreach emails	3 days	Wed 19/08/26	Fri 21/08/26	2	Sales Representative	
3.3 Contact influencers and dermatologists	2 days	Mon 24/08/26	Tue 25/08/26	3	Outreach coordinator	
3.4 Organise demo sessions	2 days	Wed 26/08/26	Thu 27/08/26	4	Sales Representative	
3.5 Prepare for trade fairs	3 days	Fri 28/08/26	Tue 01/09/26	5	Marketing Manager	
3.6 Share demo portal & materials	1 day	Wed 02/09/26	Wed 02/09/26	6	Sales Representative	
3.7 Collect client feedback	2 days	Thu 03/09/26	Fri 04/09/26	7	Marketing Analyst	
WP3 Complete	0 days	Fri 04/09/26	Fri 04/09/26	8		

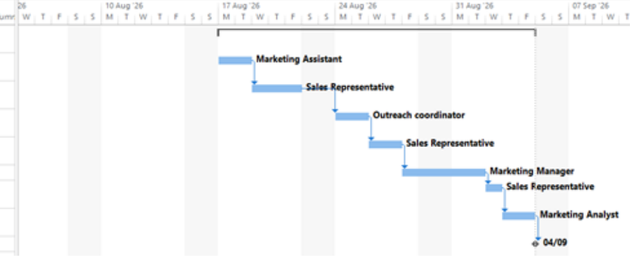

5. RESOURCES & COSTS

5. 1 Human Resources

Management & Coordination

- Marketing Manager
- Project Supervisor
- Administrator

Communication & PR

- PR Officer
- Marketing Team
- All stakeholders

Outreach & Engagement

- Outreach Coordinator
- Sales Representative

Creative Content Production

- Copywriter
- Graphic Designer
- Web Editor
- Social Media Coordinator

Marketing Strategy & Analysis

- Marketing Analyst
- Marketing Lead
- Marketing Intern
- Marketing Assistant

5. 1 Human Resources Sheet

	Resource Name	Type	Mate Label	Initials	Grc	Max. Units	Std. Rate	Ovt. Rate	Cost/Use	Accrue At	Base Calendar
1	Marketing Analyst	Work		M		100%	€40.00/hr	€0.00/hr	€0.00	Prorated	Standard
2	Marketing Lead	Work		M		100%	€45.00/hr	€0.00/hr	€0.00	Prorated	Standard
3	Marketing Intern	Work		M		100%	€20.00/hr	€0.00/hr	€0.00	Prorated	Standard
4	Marketing Manager	Work		M		100%	€50.00/hr	€0.00/hr	€0.00	Prorated	Standard
5	Marketing Team	Work		M		100%	€35.00/hr	€0.00/hr	€0.00	Prorated	Standard
6	All stakeholders	Work		A		100%	€0.00/hr	€0.00/hr	€0.00	Prorated	Standard
7	Copywriter	Work		C		100%	€28.00/hr	€0.00/hr	€0.00	Prorated	Standard
8	Graphic Designer	Work		G		100%	€30.00/hr	€0.00/hr	€0.00	Prorated	Standard
9	PR Officer	Work		P		100%	€32.00/hr	€0.00/hr	€0.00	Prorated	Standard
10	Web Editor	Work		W		100%	€25.00/hr	€0.00/hr	€0.00	Prorated	Standard
11	Administrator	Work		A		100%	€25.00/hr	€0.00/hr	€0.00	Prorated	Standard
12	Project Supervisor	Work		P		100%	€55.00/hr	€0.00/hr	€0.00	Prorated	Standard
13	Social Media Coordinator	Work		S		100%	€30.00/hr	€0.00/hr	€0.00	Prorated	Standard
14	Marketing Assistant	Work		M		100%	€35.00/hr	€0.00/hr	€0.00	Prorated	Standard
15	Outreach coordinator	Work		O		100%	€28.00/hr	€0.00/hr	€0.00	Prorated	Standard
16	Sales Representative	Work		S		100%	€35.00/hr	€0.00/hr	€0.00	Prorated	Standard

5. 1 Human Resources

Why Current Plan Is Inefficient

- Too many specialised roles
- Low utilisation across work packages
- Staff hired only for short periods
- High coordination and overhead cost
- Wasted budget on underused resources
- Tasks could be done by fewer people

Improved Resource Strategy

- Hire fewer multi-skilled workers
- Reduce number of specialised roles
- Consolidate activities under broader roles
- Increase staff utilisation and continuity
- Lower management and communication overhead
- More efficient use of budget

5. 2 Project Costs

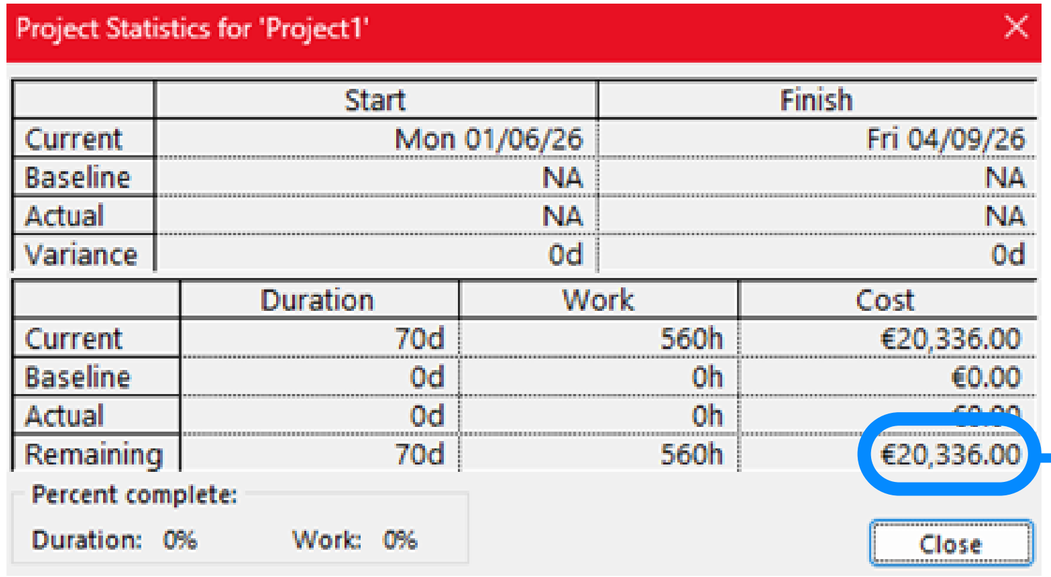

Total Human Resource Cost =
2% of € 1M budget

6. POTENTIAL RISKS

6. 1 Risks

- Data privacy and GDPR compliance
- AI may produce inaccurate analysis
- AR performance issues on devices
- Incorrect or outdated product data
- System downtime or scalability limits
- User over-reliance on app guidance
- Delays in marketing dependencies
