Project Planning

Contents

1.0 Project Brief 2

2. 0 Mind Maps for Project Planning 3

2.1 Mind Map for Marketing Plan 3

3.0 Work Breakdown Structures 4

4.0 Action Plans 5

4.1 Action Plan for Work Package 1.0 5

4.2 Action Plan for Work Package 2.0 6

4.3 Action Plan for Work Package 3.0 7

4.4 Action Plan for Work Package 4.0 8

4.5 Action Plan for Work Package 5.0 9

5.0 Project Management 10

5.1 Gantt Chart: WP1 10

5.2 Gantt Chart: WP4 10

5.3 Gantt Chart: WP2 10

5.4 Gantt Chart: WP5 10

5.5 Gantt Chart: WP3 11

5.6 Resource Sheet 11

5.7 Total Costs 11

1.0 Project Brief

The project focuses on the marketing planning for PerfectMatch, a mobile application that uses AI, AR, and smart sensors to help people get safer and more personalised beauty and self-care routines. It covers a wide range of areas including skincare, makeup, haircare, nail care, fragrances, and men's grooming.

The app includes several major features, such as ingredient safety checking (through barcode scans or uploaded photos), AI skin analysis, AR virtual makeup try-on, and the ability to compare products by safety, price, brand reputation, and sustainability. Users can also access extra tools like quizzes, progress tracking, community posts, and optional dermatologist feedback. The system is supported by a cloud-based architecture so it can handle AI analysis, AR rendering, and product database updates reliably.


While the system itself is aimed at everyday consumers, this marketing project focuses on promoting the app to business clients instead of end-users. These clients could include dermatology clinics, skincare brands, beauty retailers, and professional influencers who may want to adopt or integrate the system. The goal of the project is to plan how the system should be presented, priced, promoted, and distributed for a business environment.

2. 0 Mind Maps for Project Planning

Mind maps are a visual planning tool used to organise ideas, concepts, and project information in a clear and structured way. They help break down a project into key themes or categories, making it easier to see the overall picture immediately. In project planning, mind maps are especially useful at the early stages because they allow the project team to explore all areas of the project, identify major issues, and understand how different parts connect.

For marketing planning, a mind map helps group activities under the 5 Ps (Product, Price, Promotion, Place, and People) and highlight other important factors such as costs and competitors. This creates a foundation for identifying the main work packages and tasks that will later be developed in more detail in the Work Breakdown Structure.


2.1 Mind Map for Marketing Plan

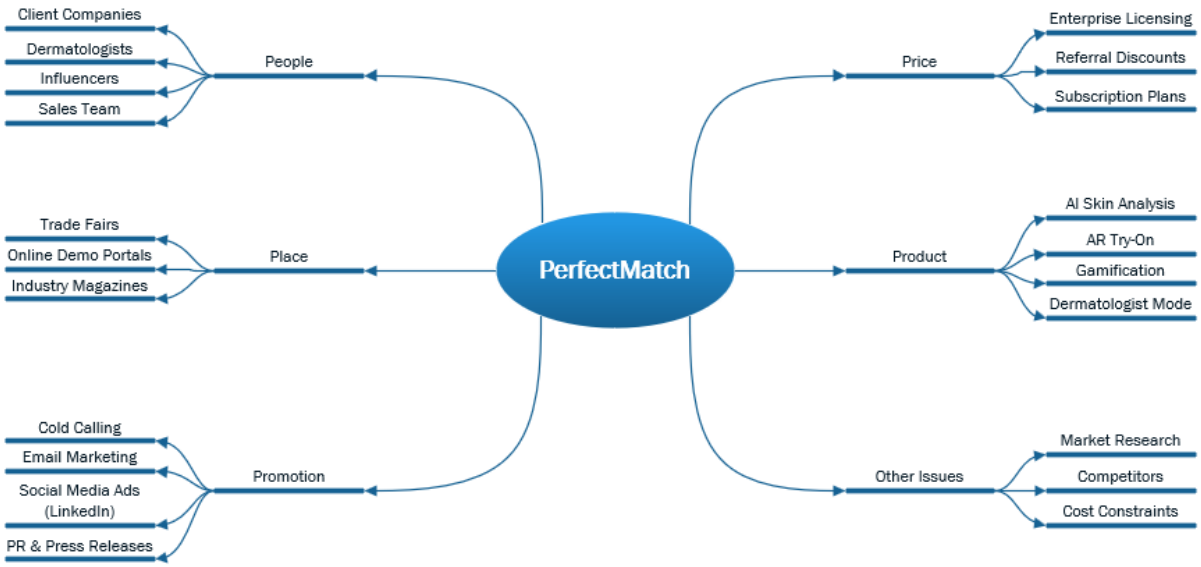

3.0 Work Breakdown Structures

A Work Breakdown Structure (WBS) is a project planning tool that breaks a project into smaller, manageable sections called work packages. It provides a clear hierarchical structure of all the major activities needed to complete the project.

In marketing planning, the WBS turns the ideas from the mind map into practical work packages, such as developing the marketing strategy, creating promotional materials, performing client outreach, and building the pricing model. Each of these work packages can then be detailed further in action plans. The WBS helps ensure that nothing important is missed and that the project is organised in a logical and efficient way.

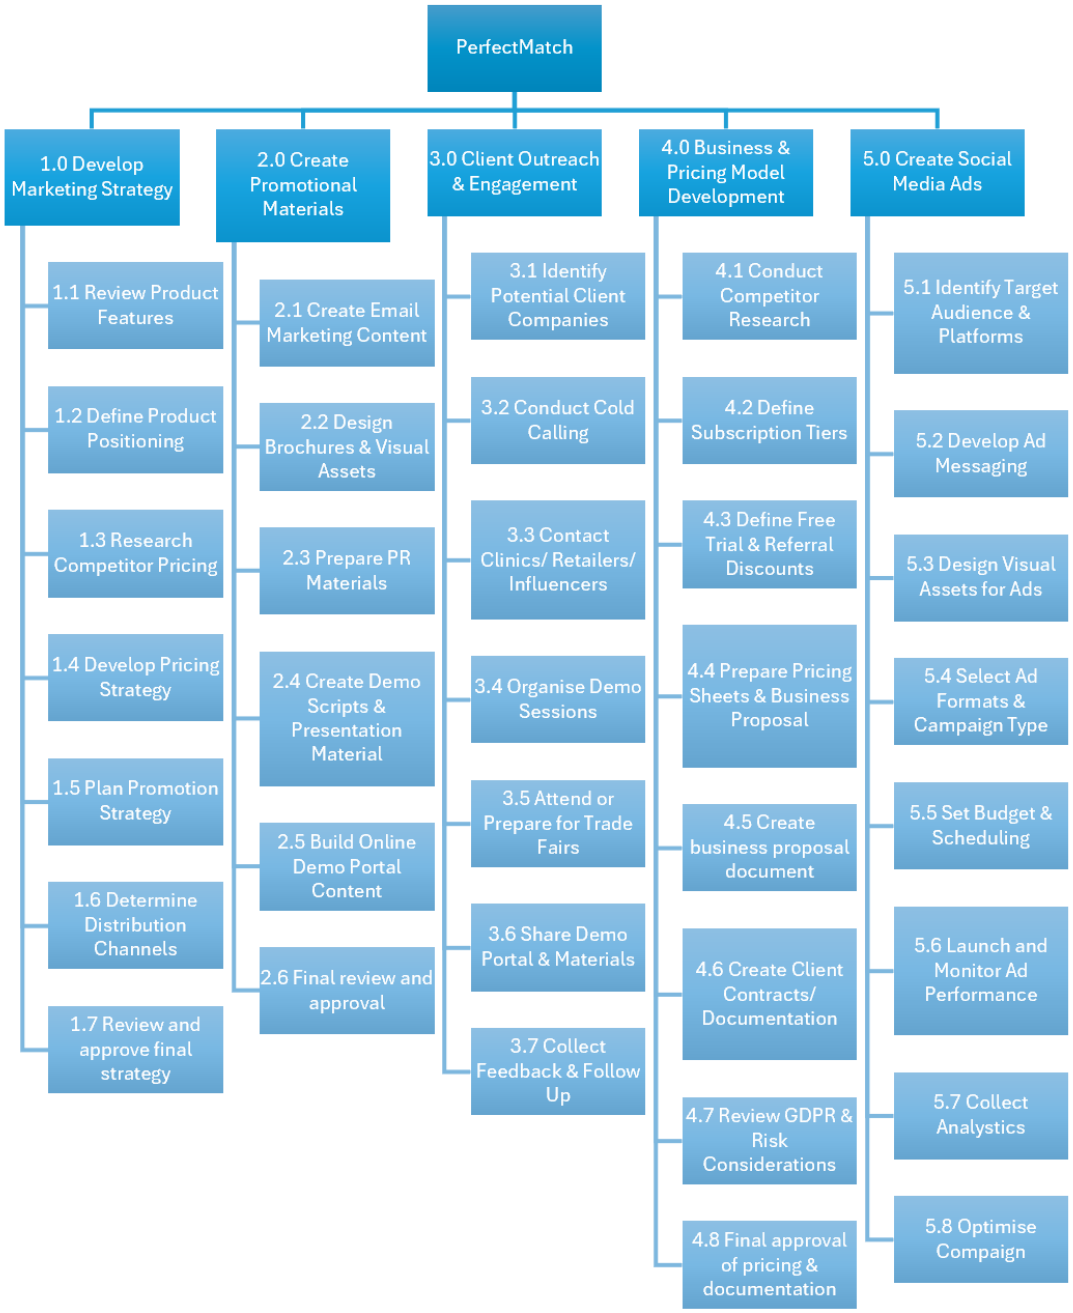

** I acknowledge that some parts of this diagram could be broken down into more actions

4.0 Action Plans

4.1 Action Plan for Work Package 1.0

Action Plan for Work Package 1.0: Develop Marketing Strategy

Deliverables on completion of Work Package

- Finalised 5P marketing strategy
- Documented product positioning
- Decided pricing structure
- Promotion plan
- Distribution plan

Measures of Accomplishments / Milestones

- Product positioning draft complete
- Pricing tiers approved
- Promotion strategy reviewed
- Distribution channels confirmed

Key constraints and Assumptions

- Assumes access to system feature documentation
- Competitor data is available
- Marketing team is available for review and approval

Number	Task	Resources	Preceding Task	Duration	Assigned to/ Responsible
1.1	Review system product features	Marketing Analyst	-	1 day	Marketing Analyst
1.2	Define product positioning	Marketing Lead	1.1	1 day	Marketing Lead
1.3	Research competitor pricing	Marketing Intern	1.2	2 days	Marketing Intern
1.4	Develop pricing strategy	Marketing Lead	1.3	2 days	Marketing Lead
1.5	Plan promotional strategy	Marketing Team	1.4	3 days	Social Media/ PR Team
1.6	Determine distribution channels	Marketing Manager	1.5	2 days	Marketing Manager
1.7	Review and approve final marketing strategy	All stakeholders	1.6	1 day	Project Supervisor

4.2 Action Plan for Work Package 2.0

Action Plan for Work Package 2.0: Create Promotional Materials

Deliverables on completion of Work Package

- Email campaign templates
- Brochures and visual assets
- PR content
- Demo scripts and presentation material
- Online demo portal content

Measures of Accomplishments / Milestones

- Visual asset pack completed
- Email templates approved
- Demo script finished
- PR content ready
- Demo portal published

Key constraints and Assumptions

- Design software available
- Access to screenshots and app assets
- Management approval required for public content

Number	Task	Resources	Preceding Task	Duration	Assigned to/ Responsible
2.1	Write email marketing content	Copywriter	-	2 days	Copywriter
2.2	Design brochures & leaflets	Graphic Designer	2.1	3 days	Graphic Designer
2.3	Prepare PR materials	PR Officer	2.2	2 days	PR Officer
2.4	Write demo script & slide deck	Marketing Lead	2.3	2 days	Marketing Lead
2.5	Build online demo portal content	Web Editor	2.4	3 days	Web Editor
2.6	Final review and approval of all materials	Marketing Manager	2.5	1 day	Marketing Manager

4.3 Action Plan for Work Package 3.0

Action Plan for Work Package 3.0: Client Outreach & Engagement

Deliverables on completion of Work Package

- Client list
- Outreach emails sent
- Cold calls completed
- Demo sessions scheduled
- Trade fair participation organised
- Client feedback collected

Measures of Accomplishments / Milestones

- Completed list of potential clients
- 50% outreach responses
- 5+ demo sessions booked
- Feedback collected from at least 3 clients

Key constraints and Assumptions

- Email platform available
- Up-to-date contact lists
- Clients respond within expected timeframe
- Trade fair availability confirmed

Number	Task	Resources	Preceding Task	Duration	Assigned to/ Responsible
3.1	Identify potential business clients	Marketing Assistant	-	2 days	Marketing Assistant
3.2	Conduct cold calling & outreach emails	Sales Team	3.1	3 days	Sales Representative
3.3	Contact influencers and dermatologists	Outreach Coordinator	3.2	2 days	Outreach Coordinator
3.4	Organise demo sessions	Sales Team	3.3	2 days	Sales Representative
3.5	Prepare for trade fairs	Marketing Manager	3.4	3 days	Marketing Manager
3.6	Share demo portal & materials	Sales Team	3.5	1 day	Sales Representative
3.7	Collect client feedback	Marketing Analyst	3.6	2 days	Marketing Analyst

4.4 Action Plan for Work Package 4.0

Action Plan for Work Package 4.0: Business & Pricing Model Development

Deliverables on completion of Work Package

- Completed competitor pricing analysis
- Defined subscription tiers
- Finalised free-trial and referral discount rules
- Pricing sheets prepared for clients
- Business proposal document
- Draft client contract templates
- Risk and GDPR compliance review

Measures of Accomplishments / Milestones

- Competitor research document completed
- Subscription tiers approved
- Free trial and referral discount policies finalised
- Pricing sheets reviewed and signed off
- Business proposal first draft complete
- GDPR and risk analysis completed

Key constraints and Assumptions

- Access to competitor pricing information is available online
- Pricing decisions require approval from a project supervisor
- Legal compliance cannot be fully confirmed without expert review
- Assumes access to GDPR guidelines and documentation

Number	Task	Resources	Preceding Task	Duration	Assigned to/ Responsible
4.1	Conduct competitor pricing research	Marketing Analyst	-	2 days	Marketing Analyst
4.2	Define subscription tiers	Marketing Lead	4.1	2 days	Marketing Lead
4.3	Define free trial & referral discount policies	Marketing Lead	4.2	2 days	Marketing Lead
4.4	Prepare pricing sheets	Marketing Analyst	4.3	2 days	Marketing Analyst
4.5	Create business proposal document	Marketing Manager	4.4	3 days	Marketing Manager
4.6	Draft client contract templates	Administrator/ Analyst	4.5	2 days	Administrator
4.7	Review GDPR compliance & identify risks	Project Supervisor/ Analyst	4.6	2 days	Project Supervisor
4.8	Final approval of pricing & business documentation	All stakeholders	4.7	1 day	Supervisor/ Manager

4.5 Action Plan for Work Package 5.0

Action Plan for Work Package 5.0: Create Social Media Ads

Deliverables on completion of Work Package

- Identified target audience and selected platforms
- Approved ad messaging
- Completed visual assets for ads
- Chosen campaign formats and objectives
- Defined ad budget and scheduling plan
- Live ad campaigns running
- Analytics report collected
- Optimisation adjustments implemented

Measures of Accomplishments / Milestones

- Target audience defined
- Ad messages drafted and approved
- Visual designs completed
- Budget and schedule finalised
- Campaign launched
- Performance analytics collected
- Campaign optimisation completed

Key constraints and Assumptions

- Access to social media ad platforms (LinkedIn/ Instagram)
- Design software and brand assets available
- Budget approved by the marketing manager
- Analytics tools accessible (LinkedIn Campaign Manager, Meta Ads Manager)
- Assumes timely approvals to avoid campaign delays

Number	Task	Resources	Preceding Task	Duration	Assigned to/ Responsible
5.1	Identify target audience & select platforms	Analyst	-	1 day	Marketing Analyst
5.2	Develop ad messaging	Copywriter	5.1	2 days	Copywriter
5.3	Design visual assets for ads	Graphic Designer	5.2	3 days	Graphic Designer
5.4	Select ad formats & campaign type	Marketing Lead	5.3	1 day	Marketing Lead
5.5	Set budget & scheduling	Marketing Manager	5.4	1 day	Marketing Manager
5.6	Launch ad campaign & monitor performance	Social Media Coordinator	5.5	2 days	Social Media Coordinator
5.7	Collect analytics	Analyst	5.6	2 days	Marketing Analyst
5.8	Optimise campaign based on analytics	Social Media Coordinator	5.7	2 days	Social Media Coordinator


5.0 Project Management

The Work Packages are scheduled based on logical dependencies. WP1 (Marketing Strategy) must be completed first because it defines the direction for all later tasks. WP4 (Pricing & Business Model) follows, as pricing decisions depend on the strategy. Once both are in place, WP2 (Promotional Materials) can be created using the finalised messaging and pricing. After promotional materials are ready, WP5 (Social Media Ads) can be developed. WP3 (Client Outreach) comes last, because outreach requires the completed promotional materials, pricing documents, and demo content.

Overall order: WP1 → WP4 → WP2 → WP5 → WP3.


5.1 Gantt Chart: WP1

Task Name	Duration	Start	Finish	Predecesso	Resource Names
WP1 Develop Marketing Strategy	**12 days**	**Mon 01/06/26**	**Tue 16/06/26**		
1.1 Review system product features	1 day	Mon 01/06/26	Mon 01/06/26		Marketing Analyst
1.2 Define product positioning	1 day	Tue 02/06/26	Tue 02/06/26	2	Marketing Lead
1.3 Research competitor pricing	2 days	Wed 03/06/26	Thu 04/06/26	3	Marketing Intern
1.4 Develop pricing strategy	2 days	Fri 05/06/26	Mon 08/06/26	4	Marketing Lead
1.5 Plan promotional strategy	3 days	Tue 09/06/26	Thu 11/06/26	5	Marketing Team
1.6 Determine distribution channels	2 days	Fri 12/06/26	Mon 15/06/26	6	Marketing Manager
1.7 Review and approve final marketing strategy	1 day	Tue 16/06/26	Tue 16/06/26	7	All stakeholders
WP1 Complete	0 days	Tue 16/06/26	Tue 16/06/26	8	

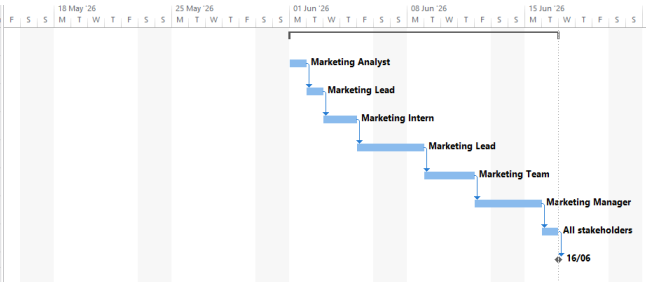


5.2 Gantt Chart: WP4

Task Name	Duration	Start	Finish	Predecesso	Resource Names
WP4 Business & Pricing Model Development	**16 days?**	**Wed 17/06/26**	**Wed 08/07/26**		
4.1 Conduct competitor pricing research	2 days	Wed 17/06/26	Thu 18/06/26		Marketing Analyst
4.2 Define subscription tie	2 days	Fri 19/06/26	Mon 22/06/26	2	Marketing Lead
4.3 Define free trial & referral discount policies	2 days	Tue 23/06/26	Wed 24/06/26	3	Marketing Lead
4.4 Prepare pricing sheets	2 days	Thu 25/06/26	Fri 26/06/26	4	Marketing Analy
4.5 Create business proposal document	3 days	Mon 29/06/26	Wed 01/07/26	5	Marketing Manager
4.6 Draft client contract templates	2 days	Thu 02/07/26	Fri 03/07/26	6	Administrator
4.7 Review GDPR compliance & identify	2 days	Mon 06/07/26	Tue 07/07/26	7	Project Supervisor
4.8 Final approval of pricing & business	1 day	Wed 08/07/26	Wed 08/07/26	8	All stakeholders
WP4 Complete	0 days	Wed 08/07/26	Wed 08/07/26	9	

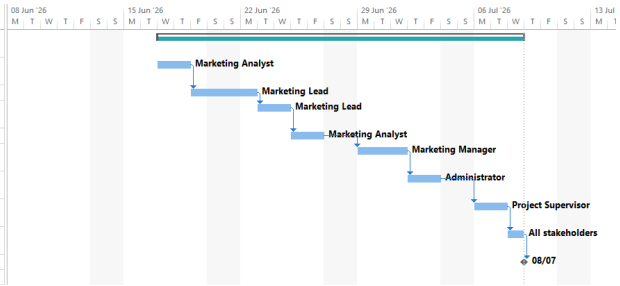


5.3 Gantt Chart: WP2

Task Name	Duration	Start	Finish	Predecesso	Resource Names
WP2 Create Promotional Material	**13 days**	**Thu 09/07/26**	**Mon 27/07/26**		
2.1 Write email marketing	2 days	Thu 09/07/26	Fri 10/07/26		Copywriter
2.2 Design brochures & leaflets	3 days	Mon 13/07/26	Wed 15/07/26	2	Graphic Designer
2.3 Prepare PR materials	2 days	Thu 16/07/26	Fri 17/07/26	3	PR Officer
2.4 Write demo script & slide deck	2 days	Mon 20/07/26	Tue 21/07/26	4	Marketing Lead
2.5 Build online demo portal content	3 days	Wed 22/07/26	Fri 24/07/26	5	Web Editor
2.6 Final review and approval of all materials	1 day	Mon 27/07/26	Mon 27/07/26	6	Marketing Manager
WP2 Complete	0 days	Mon 27/07/26	Mon 27/07/26	7	




5.4 Gantt Chart: WP5

Task Name	Duration	Start	Finish	Predecesso	Resource Names
WP5 Create Social Media Ads	**14 days**	**Tue 28/07/26**	**Fri 14/08/26**		
5.1 Identify target audience & select platforms	1 day	Tue 28/07/26	Tue 28/07/26		Marketing Analyst
5.2 Develop ad messaging	2 days	Wed 29/07/26	Thu 30/07/26	2	Copywriter
5.3 Design visual assets for ads	3 days	Fri 31/07/26	Tue 04/08/26	3	Graphic Designer
5.4 Select ad formats & campaign type	1 day	Wed 05/08/26	Wed 05/08/26	4	Marketing Lead
5.5 Set budget & scheduling	1 day	Thu 06/08/26	Thu 06/08/26	5	Marketing Manager
5.6 Launch ad campaign & monitor performance	2 days	Fri 07/08/26	Mon 10/08/26	6	Social Media Coordinator
5.7 Collect analytics	2 days	Tue 11/08/26	Wed 12/08/26	7	Marketing Analy
5.8 Optimise campaign based on analytics	2 days	Thu 13/08/26	Fri 14/08/26	8	Social Media Coordinator
WP5 Complete	0 days	Fri 14/08/26	Fri 14/08/26	9	

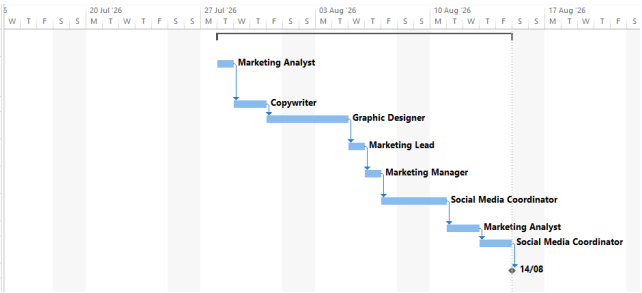

5.5 Gantt Chart: WP3

Task Name	Duration	Start	Finish	Predecesso	Resource Names	Add New Column
WP3 Client Outreach & Engagement	15 days	Mon 17/08/26	Fri 04/09/26			
3.1 Identify potential business clients	2 days	Mon 17/08/26	Tue 18/08/26		Marketing Assistant	
3.2 Conduct cold calling & outreach emails	3 days	Wed 19/08/26	Fri 21/08/26	2	Sales Representative	
3.3 Contact influencers and dermatologists	2 days	Mon 24/08/26	Tue 25/08/26	3	Outreach coordinator	
3.4 Organise demo sessions	2 days	Wed 26/08/26	Thu 27/08/26	4	Sales Representative	
3.5 Prepare for trade fairs	3 days	Fri 28/08/26	Tue 01/09/26	5	Marketing Manager	
3.6 Share demo portal & materials	1 day	Wed 02/09/26	Wed 02/09/26	6	Sales Representative	
3.7 Collect client feedback	2 days	Thu 03/09/26	Fri 04/09/26	7	Marketing Analyst	
WP3 Complete	0 days	Fri 04/09/26	Fri 04/09/26	8		

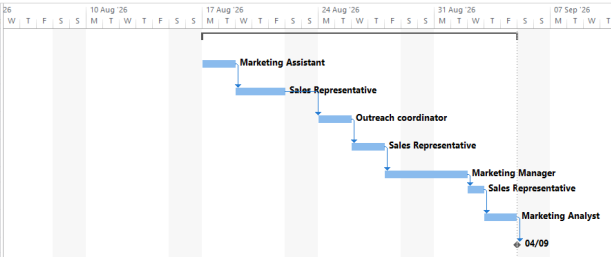

5.6 Resource Sheet

	Resource Name	Type	Mate Label	Initials	Grc	Max. Units	Std. Rate	Ovt. Rate	Cost/Use	Accrue At	Base Calendar
1	Marketing Analyst	Work		M		100%	€40.00/hr	€0.00/hr	€0.00	Prorated	Standard
2	Marketing Lead	Work		M		100%	€45.00/hr	€0.00/hr	€0.00	Prorated	Standard
3	Marketing Intern	Work		M		100%	€20.00/hr	€0.00/hr	€0.00	Prorated	Standard
4	Marketing Manager	Work		M		100%	€50.00/hr	€0.00/hr	€0.00	Prorated	Standard
5	Marketing Team	Work		M		100%	€35.00/hr	€0.00/hr	€0.00	Prorated	Standard
6	All stakeholders	Work		A		100%	€0.00/hr	€0.00/hr	€0.00	Prorated	Standard
7	Copywriter	Work		C		100%	€28.00/hr	€0.00/hr	€0.00	Prorated	Standard
8	Graphic Designer	Work		G		100%	€30.00/hr	€0.00/hr	€0.00	Prorated	Standard
9	PR Officer	Work		P		100%	€32.00/hr	€0.00/hr	€0.00	Prorated	Standard
10	Web Editor	Work		W		100%	€25.00/hr	€0.00/hr	€0.00	Prorated	Standard
11	Administrator	Work		A		100%	€25.00/hr	€0.00/hr	€0.00	Prorated	Standard
12	Project Supervisor	Work		P		100%	€55.00/hr	€0.00/hr	€0.00	Prorated	Standard
13	Social Media Coordinator	Work		S		100%	€30.00/hr	€0.00/hr	€0.00	Prorated	Standard
14	Marketing Assistant	Work		M		100%	€35.00/hr	€0.00/hr	€0.00	Prorated	Standard
15	Outreach coordinator	Work		O		100%	€28.00/hr	€0.00/hr	€0.00	Prorated	Standard
16	Sales Representative	Work		S		100%	€35.00/hr	€0.00/hr	€0.00	Prorated	Standard

5.7 Total Costs

Project Statistics for 'Project1'

	Start	Finish
Current	Mon 01/06/26	Fri 04/09/26
Baseline	NA	NA
Actual	NA	NA
Variance	0d	0d

	Duration	Work	Cost
Current	70d	560h	€20,336.00
Baseline	0d	0h	€0.00
Actual	0d	0h	€0.00
Remaining	70d	560h	€20,336.00

Percent complete:

Duration: 0% Work: 0%

Close
